

## Cloud Construction

## Clifton Park/Bellaire ES Consolidation


Monthly Progress Report - October 2020




Exterior: Front canopy soffit installation preparing for finishes.



Exterior: Playground canopies are installed.

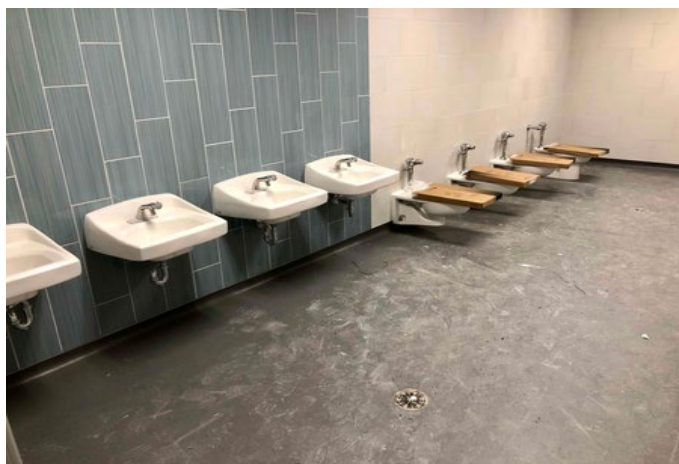

Interior: Group restroom flooring and fixtures being installed.

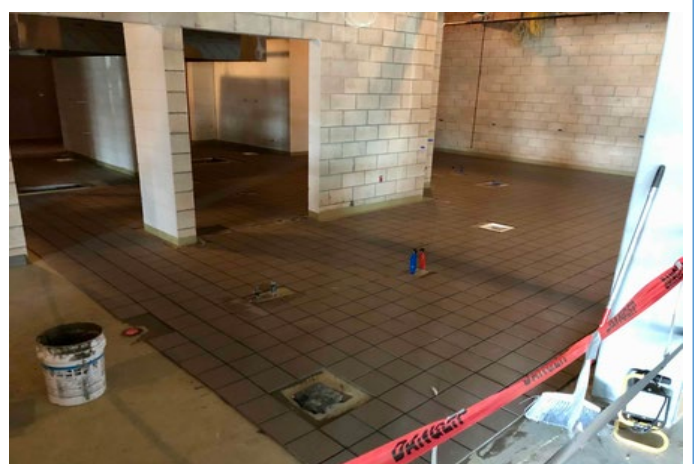

Interior: Kitchen quarry tile being installed.

### This Month's Major Activities:

- Exterior: Playground canopies installed.
- Exterior: Fencing has begun and irrigation lines are being run.
- Interior: Area 1 stone veneer installed.
- Interior: Area 4 quarry tile in kitchen.
- Interior: Casework installed 1st floor; delivered 2nd floor.

### Next Month's Major Activities:

- Exterior: Complete irrigation and begin landscaping.
- Interior: Sheet vinyl in restrooms with plumbing fixtures to follow.
- Interior: LVT at all classrooms
- Interior: Complete casework and countertops throughout.

Design Percent Complete - 100%

Construction Percent Complete - 76%
