


Site: Football stadium bleacher installation in progress.



Site: Canopy installation in progress on east side of buildings.



Site: Concrete paving placed and finished at south side of Area MNP.

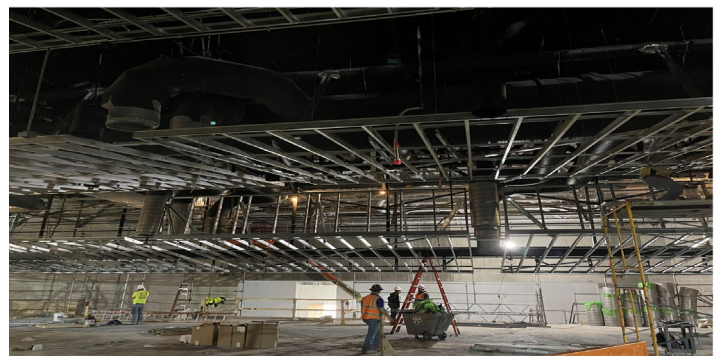

Site: Auditorium cloud framing in progress.

December Week 1 - Major Activities:

- Final Punchlist Completion A,B 1st and 2nd Floor
- Install SVF/LVT Flooring in area C/D 2nd floor
- Drop Ceiling Tile Area D Mainstreet
- Polish Concrete Floors Area D Mainstreet
- Install FRP at Mopsinks
- Trim Out MDF
- Rough Clean C,D 1st Floor
- Ice Machine Delivery/Install
- Drop Ceiling Tile Media Center
- Kitchen Storage Rack Delivery
- Pre-Punch Kitchen
- Rough Clean Kitchen Floors
- Ceiling Grid Install Fine Arts Mainstreet Corridor
- Auditorium Cloud Framing
- Above ceiling rough in MEP for auditorium
- Overhead Special Systems Rough Fine Arts
- Auditorium Lobby Recessed Strip Lighting
- Exterior masonry columns areas H,K,N
- Above Ceiling MEP at Field House/PB
- Sheetrock Walls at Pressbox
- Frame Ceilings at Field House
- East Bus Loop Canopy

Percent Design Complete: 100%

Next Week's Major Activities:

- Final Punchlist Completion A,B 1st and 2nd Floor
- Install SVF/LVT Flooring in area C/D 2nd floor
- Pre-Punch area C,D 1st and 2nd Floor
- Polish Concrete Floors Area C and D Mainstreet
- Trim Out MDF
- Rough Clean C,D 2nd Floor
- Terrazzo Treads/Landing area G Learning Stairs
- Install Athletics Wall Pads
- Install Whirlpools in Training Room
- Install Commercial Laundry Equipment in Athletics
- Final Clean Gyms and Athletics Mainstreet
- Pre-Punch Kitchen
- Ceiling Grid Install Fine Arts Mainstreet Corridor
- Trim Out Ceiling Grid Fine Arts Mainstreet Corridor
- Ceiling Grid Fine Arts Back of House Corridors
- Above ceiling rough in MEP for auditorium
- Exterior masonry columns areas H,K
- Above Ceiling MEP at Field House/PB
- Sheetrock Walls at Pressbox
- Main Entry Sidewalk
- Ballstopper Netting at Baseball and Softball

End of November Construction Complete: 83%

(% complete includes Building & Stadium Expansion)
