




Building: Area D polished concrete in progress.



Site: Main entrance concrete paving prep in progress.

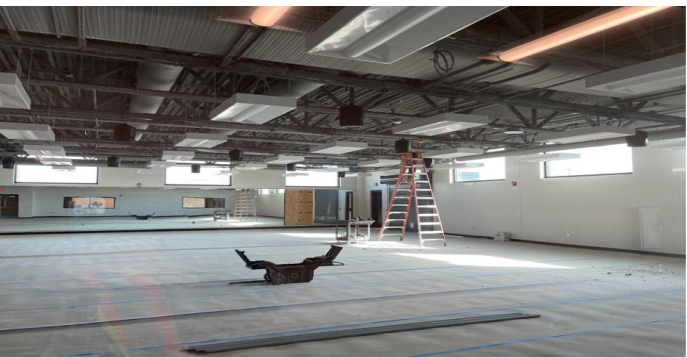

Building: Local sound system installation in progress at weight rooms.



Site: Fence mockup in progress along Chaparral Road.

December Week 2 - Major Activities:

- Final Punchlist Completion A,B 1st and 2nd Floor
- Install SVF/LVT Flooring in area C/D 2nd floor
- Pre-Punch area C,D 1st and 2nd Floor
- Polish Concrete Floors Area C and D Mainstreet
- Trim Out MDF
- Rough Clean C,D 2nd Floor
- Terrazzo Treads/Landing area G Learning Stairs
- Install Whirlpools in Training Room
- Install Commercial Laundry Equipment in Athletics
- Pre-Punch Kitchen
- Ceiling Grid Install Fine Arts Mainstreet Corridor
- Trim Out Ceiling Grid Fine Arts Mainstreet Corridor
- Ceiling Grid Fine Arts Back of House Corridors
- Above ceiling rough in MEP for auditorium
- Sheetrock Furrount walls area K Lobby
- Exterior masonry columns areas H,K
- Above Ceiling MEP at Field House/PB
- Sheetrock Walls at Pressbox
- Home Grandstands
- Angle Frame Bleachers
- Irrigation
- Decorative Fence

Percent Design Complete: 100%

Next Week's Major Activities:

- Pre-Punch area C,D 1st and 2nd Floor
- Polish Concrete Floors Area C and D Mainstreet
- Trim Out MDF
- Final Clean C,D 1st Floor
- Final Punch C,D 1st Floor
- Drop Ceiling Tile area C Mainstreet
- Drop Rulon Ceiling Tile Media Center
- Kitchen Storage Rack Installation
- Install Athletics Wall Pads
- Final Clean Gyms and Athletics Mainstreet
- Ceiling Grid Install Fine Arts Back of House Corridor
- Frame Ceiling Auditorium Lobby
- Above ceiling rough in MEP for auditorium
- Overhead special systems rough Arts Mainstreet
- Overhead special systems rough Auditorium Lobby
- Install Display Cases
- Exterior masonry columns areas H,K
- Above Ceiling MEP at Field House/PB
- Sheetrock Walls at Pressbox
- Visitor Grandstands
- Irrigation
- Sidewalks

End of November Construction Complete: 83%

(% complete includes Building & Stadium Expansion)
