



**Building:** Area C/D being completed and prepped for punch.



**Building:** Area G Commons terrazzo stairs being installed.

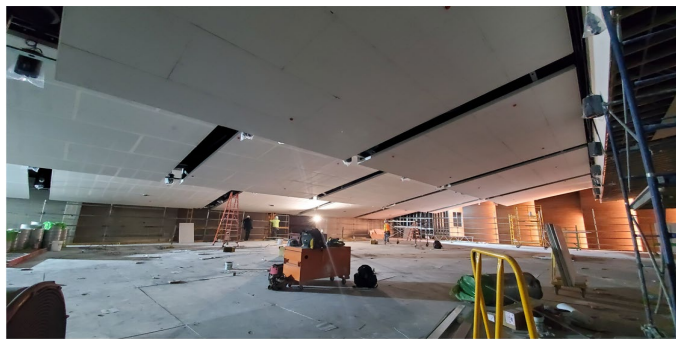

**Building:** Auditorium ceiling clouds being sheetrocked & prepped for paint.

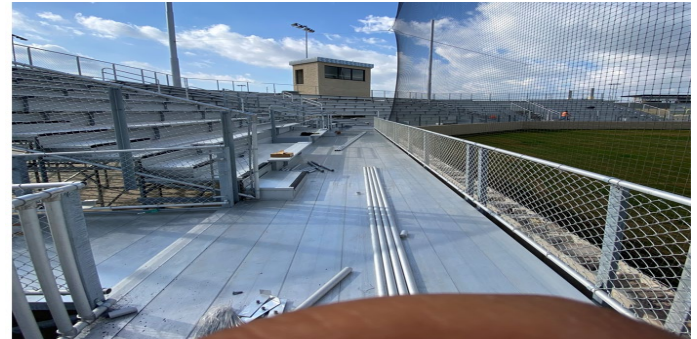

**Site:** Baseball angle frame bleachers installation in progress.

**December Week 5 - Major Activities:**

- Install Tile Base Mockup MNP
- Final Clean C/D
- Pre-punch C/D
- Complete Polish Concrete Area C Mainstreet
- Trim Out MDF
- Final Clean Gyms and Athletics Mainstreet
- Ceramic Tile E Learning Stair
- Drop Rulon Ceiling Tile Media Center
- Pre-punch Kitchen
- Trim out Ceiling Grid Fine Arts Back of House Corridor
- Frame/Sheetrock Ceiling Auditorium Lobby
- Above ceiling rough in MEP for auditorium
- Overhead special systems Arts Mainstreet
- Overhead special systems Auditorium Lobby
- Install Display Cases
- Exterior masonry columns areas G/K
- Above Ceiling MEP at Field House/PB
- T/F/P Walls at Pressbox
- Irrigation
- Sidewalks
- Angle Frame Bleachers
- Walkway Canopies

**Percent Design Complete: 100%**

**Next Week's Major Activities:**

- Folding Partitions D/G
- Final Punch C1/D1
- Final Punch Athletics Main Street and ROTC
- Final Punch Gyms
- Final Punch Kitchen
- Install Ceiling Grid area G Learning Stairs
- Install Tile Base C/D/M/N/P
- Polish Concrete Floors Area G Commons
- Trim Out MDF
- Trim out Ceiling Grid Fine Arts Back of House Corridor
- Sheetrock Auditorium Lobby Ceiling/Restrooms
- Sheetrock/Tape/Float/Paint Auditorium Ceiling
- Overhead special systems Arts Mainstreet
- Overhead special systems Auditorium Lobby
- Exterior masonry columns areas G/K
- Above Ceiling MEP at Field House/PB
- T/F/P Walls at Pressbox
- Irrigation
- Sidewalks
- Angle Frame Bleachers

**End of November Construction Complete: 83%**

*(% complete includes Building & Stadium Expansion)*
