




Building: Polished concrete slab area being prepped for place and finish.



Building: Mainstreet Corridor base installation in progress.

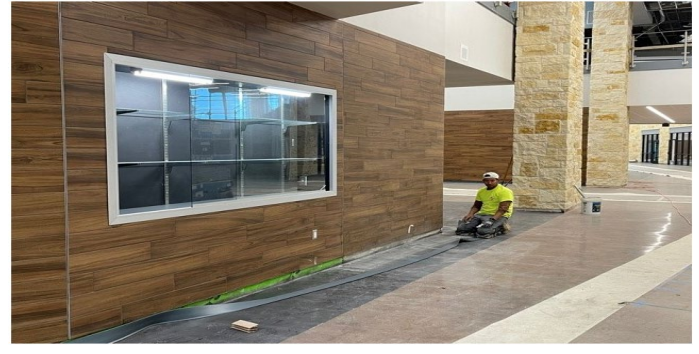

Building: Soffit panel installation in progress at high roof areas.



Site: Scoreboard framing and catwalk being installed.

January Week 4 - Major Activities:

- Trim Out MDF
- Final Punch Athletics (Locker Areas)
- Sheetrock Furrdown Above Area G Learning Stairs
- Terrazzo Treads Area G Learning Stairs
- Commissioning Areas A-F
- Pre-Punch Media Center
- Startup Remaining RTUs (Areas J and K)
- Continue RFI 196 in Dance Room and Start Area J
- Complete Terrazzo Treads Area G Learning Stairs
- Complete Flooring at D2 Above Area G Learning Stairs
- Interior Masonry Topout Metal Wrap
- Overhead Roughin Fine Arts Mainstreet
- Overhead Roughin Auditorium Lobby
- Theatre Curtain Rigging Layout
- Above Ceiling MEP at Field House/PB
- Sheetrock Ceilings at Field House
- Grid Ceilings at PB
- Irrigation
- Sidewalks
- Visitor Grandstands at Football

Percent Design Complete: 100%

Next Week's Major Activities:

- Trim Out MDF
- Final Punch Athletics (Locker Areas)
- Water Testing Areas C/D and Complete Areas A/B
- Sheetrock Furrdown Above Area G Learning Stairs
- Terrazzo Treads Area E Learning Stairs
- Commissioning Areas A-F
- Complete Startup of Remaining RTUs (Areas J and K)
- Continue RFI 196 in Area J
- Complete Flooring at D2 Above Area G Learning Stairs
- Dance Room Flooring
- Interior Masonry Topout Metal Wrap
- Final Paint Area L
- Overhead Roughin Fine Arts Mainstreet
- Drop Ceiling Tile in High Ceilings Area J
- Overhead Roughin Auditorium Lobby
- Theatre Curtain Rigging Install
- Above Ceiling MEP at Field House/PB
- Tape/Float/Paint Ceilings at Field House
- Elevator at PB
- Irrigation
- Sidewalks
- Visitor Grandstands at Football

End of December Construction Complete: 85%

(% complete includes Building & Stadium Expansion)
