


**Building:** Area A-F roofing being cleaned for punch and completion.



**Building:** Scoreboards installed at Basketballs Gyms.

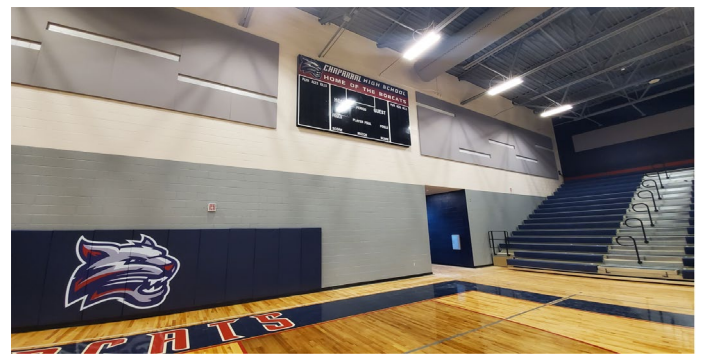

**Building:** CPR 81 tier seating change being installed at athletics.



**Site:** SOD being installed and landscaping being completed at main entry.

**April Week 3 - Major Activities:**

- Owner Furniture Stocking A/B/C/D/E/F
- Pre-Punch Roof and Roof Cleaning (All areas)
- Closeout Punchlist Areas M/N/P
- CPR 61 (Dryer Vents) J/N/P
- Test/Balance Areas G/H/M/N/P
- Metal Soffit Roof Area B6
- Pre-punch areas H/J/L
- Pre-punch Building Exterior
- Install/Adjust Doors and Door Hardware J/K/L
- Casework Area J/K
- Above Ceiling Punch Drama Classroom/Offices/Area K
- Theatre Curtain Rigging Install - Battens
- Electrical Rough-in Stage Apron/Edge
- PLAM Installation Radius Walls at Stage Wings
- Decorative Railing Installation H/K
- Irrigation
- Sidewalks/Paving
- Metal Wall Panels at PB/Field House
- Toilet Partitions at Field House
- Final Paint Field House
- Track Surfacing
- Sod North and East Sides of Main Building

**Percent Design Complete: 100%**

**Next Week's Major Activities:**

- Owner Furniture Stocking A/B/C/D/E/F
- Tile Base M/N/P Mainstreet Corridor and Auditorium
- Final Punch Roof (All Areas)
- Test/Balance Areas M/N/P
- Outdoor Basketball Court Striping
- Metal Soffit Roof Area B6
- Final Punch Areas H/J/L
- Blackbox Flooring
- Blackout Stage Area
- Casework Area K
- Above Ceiling Punch Drama Classroom/Offices/Area K
- Theatre Curtain Rigging Install - Battens
- Concrete Polishing and Sealing Area J/K/L
- PLAM Installation Radius Walls at Stage Wings
- Decorative Railing Installation H/K
- Irrigation
- Sidewalks/Paving
- Metal Siding at PB/Field House
- Track Surfacing
- Electrical at Football Video Board and Scoreboard
- Chainlink Fencing
- Punch Tennis and Field Concessions (Building R)

**End of February Construction Complete: 93%**

*(% complete includes Building & Stadium Expansion)*
