




Building: Black box room flooring installed and lighting being terminated and tested.



Building: Auditorium lobby glass railing system nearing completion.

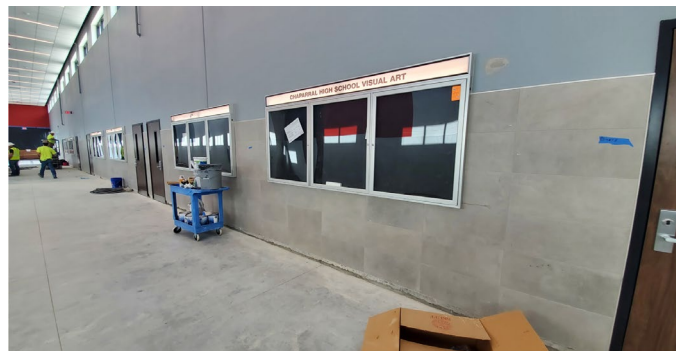

Building: Art display cases being installed and electrical terminated.



Site: Digital video board installed and terminated at site marquee sign.

April Week 4 - Major Activities:

- Owner Furniture Stocking A/B/C/D/E/F
- Pre-Punch Roof and Roof Cleaning (All areas)
- Closeout Punchlist Areas M/N/P
- Test/Balance Areas G/H/L/M/N/P
- Black Box Flooring Installation
- Kitchen Health Inspection
- Final Punch areas H/L
- Pre-punch Building Exterior
- Install/Adjust Doors and Door Hardware J/K
- Casework Area J/K
- Auditorium Carpet Area K
- Blackout Stage
- Concrete Polishing Area J Back of House
- PLAM Installation Radius Walls at Stage Wings
- Auditorium Wood Wall Finish (Back Wall)
- Decorative Railing Installation H/K
- Irrigation
- Sidewalks/Paving
- Metal Wall Panels at PB/Field House
- Toilet Partitions at Field House
- Final Paint Field House
- Track Surfacing

Percent Design Complete: 100%

Next Week's Major Activities:

- Owner Furniture Stocking A/B/C/D/E/F
- Tile Base M/N/P Mainstreet Corridor and Auditorium
- Final Punch Roof (Manufacture)
- Test/Balance Areas G/H/L/M/N/P
- Outdoor Basketball Court Striping
- Metal Soffit
- Final Punch Areas J
- Casework Area J/K
- Above Ceiling Punch Drama Classroom/Offices/Area K
- Fire Curtain and Smoke Pocket Installation
- Concrete Polishing and Sealing Area J/K/L
- PLAM Installation Radius Walls at Stage Wings
- Decorative Railing Installation H/K
- Kitchen Hood Testing
- Closeout Punchlist Items M/N/P/G/H/L
- Irrigation
- Sidewalks/Paving
- Metal Siding at PB/Field House
- Track Surfacing/Striping
- Chainlink/Ameristar Fencing
- Baseball and Softball Pressbox Finish Out
- FCU's at Pressbox

End of February Construction Complete: 93%

(% complete includes Building & Stadium Expansion)
