




Building: Roof decking Sec 5 & 6 install



Sections 3: Began window install, stone work continues.



Section 4: Roof membrane install over café & PE.

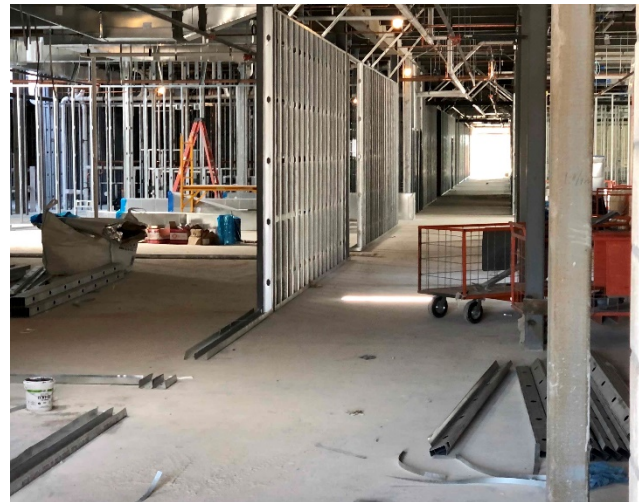

Section 2 & 3: Interior framing has begun.

This Month's Major Activities:

- Section 2 & 3: Began framing interior and MEP rough in
- Section 2 & 3: Window install & stonework
- Section 4: Roof install
- Sections 5 & 6: Decking & joists installed

Next Month's Major Activities:

- Section 1: Begin steel & roof decking
- Sections 2 & 3: Continue interior framing and MEP rough in.
- Sections 5 & 6: Main roof installation
- Sections 2 & 3: Continue stonework around building

Design Percent Complete – 100%

Construction Percent Complete – 41.93%
