

## Cloud Construction

## Pershing Park/Sugar Loaf ES Consolidation

Monthly Progress Report - October 2020




Interior: Logo signs are installed in both cafe and main hall.



Interior: Kitchen serving line is installed and protected.



Exterior: All landscaping and sod has been installed.

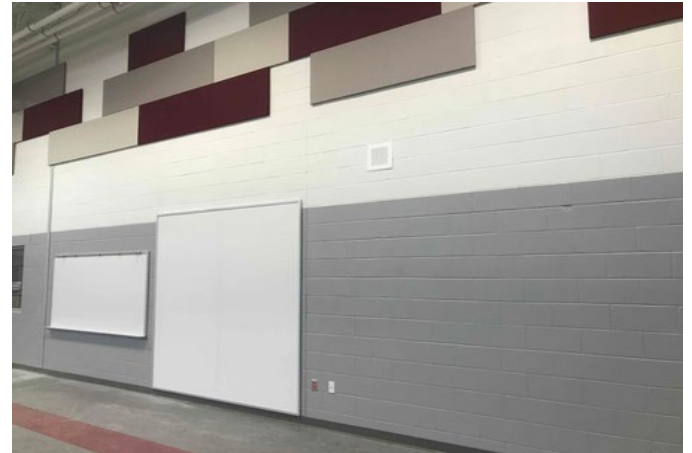

Interior: Final sound boards installed in cafe & PE.

### This Month's Major Activities:

- Exterior: Landscaping fully installed.
- Exterior: Parking lot cleaning and striping.
- Interior: Final finishes installed.
- Interior: Serving line and kitchen install completed.

### Next Month's Major Activities:

- Exterior: Punch items.
- Interior: Punch items.
- Interior: Final cleaning.
- Interior: Final inspections from city for occupancy.

Design Percent Complete - 100%

Construction Percent Complete - 85.7%
