




Exterior: Roof top HVAC units all completed.



Exterior: Area 4 stone veneer has begun along west side.

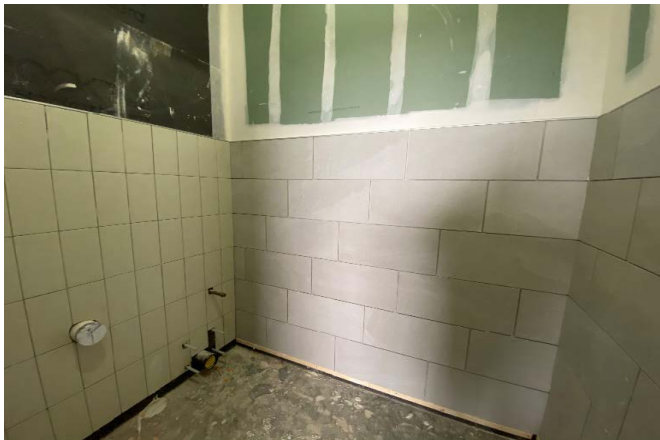

Interior: Area 3 restrooms have begun ceramic wall tile.



Exterior: Working through flashing and install of acoustic windows to begin.

This Month's Major Activities:

- Exterior: Began stone & brick veneer.
- Exterior: Complete roof and RTU installation.
- Interior: Complete in wall rough in and begin sheetrock.
- Interior: Begin ceramic tile in restrooms and prepare hallways.

Next Month's Major Activities:

- Exterior: Continue stone veneer around building
- Exterior: Begin install of acoustic windows
- Exterior: Complete remaining high roof in Area 1.
- Interior: Continue sheetrock and tape/float/paint Areas 5 & 6..
- Interior: Install kitchen vent hoods.
