


Bartlett Cocke Construction

Elementary School No. 36 Monthly Progress Report - July 2021



Exterior: Hydromulch and watering to establish grass.

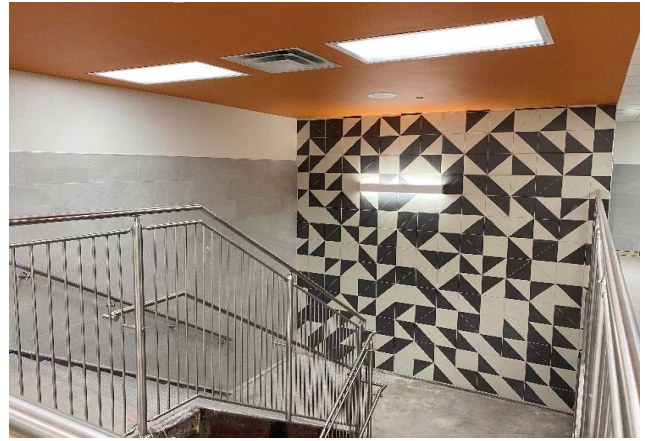

Interior: Main stairwell back wall.



Interior: Main front hallway.



Interior: Campus dedication and meet the teacher.

This Month's Major Activities:

- Exterior: Completed install of landscaping.
- Exterior: Received Certificate of Occupancy.

Next Month's Major Activities:

- Exterior: Continue to monitor the growth of hydromulched area.
- Interior: Punch list items to complete
- Interior: Commissioning to be performed.
- Immediate response to all warranty items.

Design Percent Complete - 100%

Construction Percent Complete - 87.1%
