




**Site:** Rubber pellet infill being placed in football field turf.



**Site:** Competition Football Stadium lighting being installed.

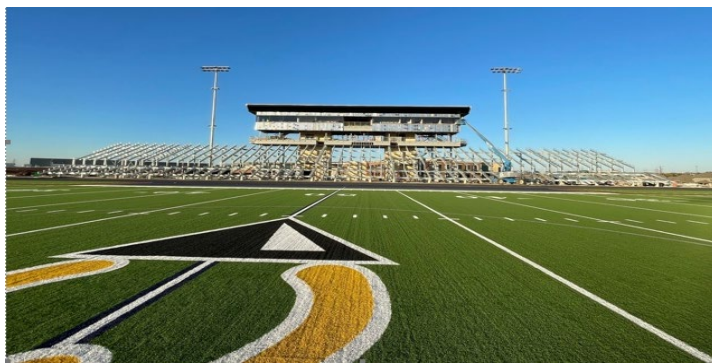

**Site:** Stadium bleacher framing installation in progress.



**Site:** Football Pressbox glazing being installed.

### November Week 2 - Major Activities:

- Final Punch A,B 1st and 2nd floor
- Install SVF/LVT flooring in area C/D 2nd floor
- Trim out ceiling grid C,D mainstreet
- Final Paint C/D 1st floor
- Ceiling grid area E learning stairs
- Local Sound System Install Area G
- Ceiling Trim Out Media Center
- Quarry Tile Walk-in Freezer/Cooler
- Kitchen Equipment Terminations
- Grid ceiling trim out in area L,J
- Install lockers in kitchen and arts rooms
- Above ceiling rough in MEP for auditorium
- Overhead special systems rough Arts Mainstreet
- Overhead special systems rough Auditorium Lobby
- Furrout walls area K Lobby
- Exterior masonry columns areas C,D,G,H,K,N
- Above Ceiling MEP at Field House
- Sheetrock Walls at Pressbox
- Curtain Wall Glass at Pressbox
- Home Grandstands
- Musco Football Lighting

**Percent Design Complete: 100%**

### Next Week's Major Activities:

- Final Punch A,B 1st and 2nd floor
- Install SVF/LVT Flooring in area C/D 2nd floor
- Ceiling Trim Out C,D mainstreet
- Final Paint C/D 1st Floor
- Ceiling Trim Out Area E Learning Stairs
- Interior Masonry Column Topout Framing area G
- Drop Ceiling Tile Media Center
- Kitchen Storage Rack Delivery
- Rough Clean Kitchen Floors
- Ceiling Grid Install Fine Arts Mainstreet Corridor
- Install lockers in kitchen and arts rooms
- Above ceiling rough in MEP for auditorium
- Overhead special systems rough Arts Mainstreet
- Overhead special systems rough Auditorium Lobby
- Exterior masonry columns areas C,D,G,H,K,N
- Above Ceiling MEP at Field House
- Sheetrock Walls at Pressbox
- Home Grandstands
- Sod Athletic Fields
- Frame Ceilings at Field House

**End of October Construction Complete: 80%**

*(% complete includes Building & Stadium Expansion)*
