




Site: Irrigation installation in progress at west side of building.



Building: Auditorium learning stairs are complete.

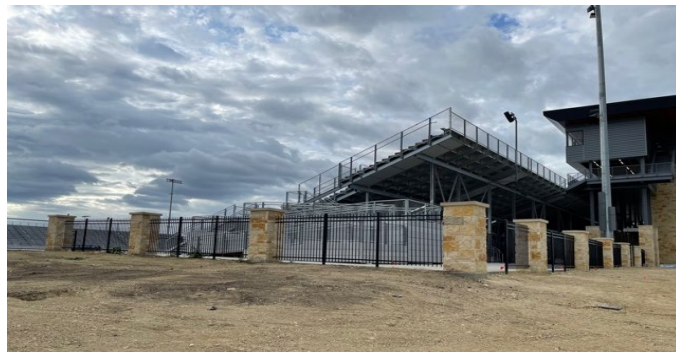

Site: Football field ornamental fencing installation in progress.



Site: Neighborhood access sidewalk being formed for concrete.

June Week 1 - Major Activities:

- Owner Furniture Stocking A-F/G/M/N/P
- Closeout Punchlist Items All Areas Except K
- Pre Punch Roof
- Exterior Architectural Pre-Punch
- Exterior Metal Soffit and Wall Panels
- Test and Balance Completing in all Areas
- Tile Base Installation Auditorium Lobby
- Learning Stair Tile Installation Auditorium Lobby
- Final Punch Auditorium/Lobby/Fine Arts Corridors
- Orchestra Shell and Tower Installation
- Paint Structure Set Shop/Mezzanine/Storage
- Tape Float and Paint Pressbox
- Chainlink Fencing
- Installing Ameristar
- Grid Ceiling Installed at PB
- Forming Sidewalk between houses
- Finishing irrigation
- Adjuster coming for elevator in pressbox
- Punched fields

Percent Design Complete: 100%

Next Week's Major Activities:

- Owner Furniture Stocking A-F/G/M/N/P
- Closeout Punchlist Items All Areas Except K
- Pre Punch Roof
- Commissioning All Areas Except K
- Exterior Metal Soffit and Wall Panels
- Final Punch Auditorium/Lobby/Fine Arts Corridors
- Fire Curtain Installation
- Orchestra Shell and Tower Installation
- Commercial and Residential Hood Testing
- Set shop/Mezz/Storage Structure Paint
- Sealed Concrete Remainder of Area K
- Landscape fine grading
- Top-dress of Grass Fields
- Mowstrip
- Metal Siding at PB/Field House
- Chainlink/Ameristar Fencing
- Grading/ Topsoil South West Area
- Laying SOD
- Pouring sidewalks/concrete punch

End of May Construction Complete: 95%

(% complete includes Building & Stadium Expansion)
